

blynt

JIRA & CONFLUENCE AGILE WORKFLOW & GOVERNANCE SPECIFICATION

Project Delivery Framework • 50-Phase Epic Hierarchy • State Machine Transitions
Quality Gates (DoR & DoD) • Confluence Space Architecture • GitHub & CI/CD Smart Automations
Authoritative Engineering Delivery Manual • October 2026

Project Delivery Governance Scope

This standalone manual establishes the standard operating procedures for Jira Software and Confluence project delivery across the blynt engineering team. It defines the issue hierarchy, workflow states, quality gates, and automated release hooks.

Document Ref: BLYNT-PMO-WORKFLOW-V1
System Name: blynt (Internal Code: Ledgerline)
Tooling Stack: Atlassian Jira Software Cloud • Confluence Cloud • GitHub Enterprise
Agile Methodology: Scrum (2-Week Iterations) & Continuous Delivery (Kanban Hotfixes)
Issue Hierarchy: Initiative -> Epic (50 Phases) -> Story / Task / Bug -> Sub-Task
Quality Gates: Definition of Ready (DoR) • 26 CI Test Suites • Definition of Done (DoD)
Classification: Confidential Engineering Delivery & Operations Manual

blynt — Jira & Confluence Agile Workflow & Governance Specification

Document Classification: Engineering Delivery Governance & Project Management

Target Systems: Atlassian Jira Software, Confluence Cloud, GitHub Enterprise CI/CD

Coverage Scope: 50-Phase Implementation Governance, State Machine Transitions, DoD/DoR Quality Gates

Version: 1.0 Production Readiness

Document Ref: `BLYNT-PMO-WORKFLOW-V1`

Table of Contents

- **1. Strategic Project Governance & Ecosystem Architecture**
- 1.1 The Jira + Confluence + GitHub Unified Delivery Pipeline
- 1.2 Confluence as the Authoritative Single Source of Truth (SSOT)
- 1.3 Jira as the Agile Execution Engine
- 1.4 Bi-Directional Linking Strategy
- **2. Issue Hierarchy & The 50-Phase Epic Architecture**
- 2.1 The 4-Tier Hierarchy: Initiative -> Epic -> Standard Issue -> Sub-Task
- 2.2 Mapping the 50 Phases into Jira Epics (`BLYNT-EPIC-01` to `BLYNT-EPIC-50`)
- 2.3 Issue Types & Taxonomy (Story, Task, Bug, Hotfix)
- **3. The Jira Issue Lifecycle & State Machine**
- 3.1 Visual Workflow State Machine Diagram
- 3.2 State Transition Definitions & Progression Rules
- 3.3 The Hotfix & Emergency Incident Workflow (SEV-1 / SEV-2)
- **4. Quality Gatekeepers: Definition of Ready & Definition of Done**
- 4.1 Definition of Ready (DoR) Gatekeeper Checklist
- 4.2 Pull Request Quality Gate & CI Automation
- 4.3 Definition of Done (DoD) Sign-Off Criteria
- **5. Confluence Space Architecture & Page Templates**
- 5.1 Confluence Space Structure (`ENG`, `PROD`, `QA`, `SEC`, `OPS`)
- 5.2 Standard Product Requirement Document (PRD) Template
- 5.3 Architectural Decision Record (ADR) Template
- 5.4 Post-Mortem Incident Template
- **6. Agile Ceremonies, Story Point Estimation & Sprint Cadence**
- 6.1 2-Week Sprint Schedule & Cadence
- 6.2 Story Pointing & Modified Fibonacci Sizing

- 6.3 Sprint Planning, Standups, Demos & Retrospectives
- **7. Jira Smart Automations & Webhooks**
- 7.1 Automated State Transitions via GitHub Webhooks
- 7.2 Slack PagerDuty Alerting for Critical Financial Defects
- 7.3 Confluence Documentation Synchronizers

1. Strategic Project Governance & Ecosystem Architecture

For an institutional financial platform where every calculation has legal and statutory ramifications, engineering delivery cannot be chaotic. The Jira and Confluence workflow provides end-to-end traceability from initial business requirement to production deployment.

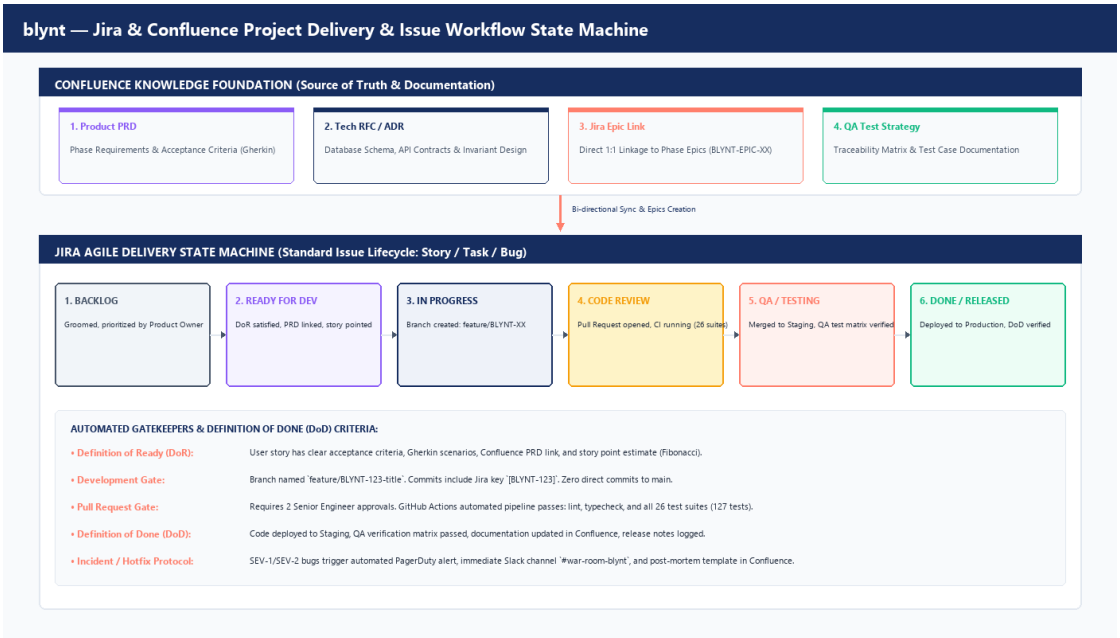


Figure Workflow - Jira and Confluence project delivery and state machine diagram

1.1 The Jira + Confluence + GitHub Unified Delivery Pipeline

```
[ CONFLUENCE: Product PRD / Tech RFC ]
             │ (1:1 Document Link)
             ▼
[ JIRA: Phase Epic (BLYNT-EPIC-XX) ]
             │ (Decomposed into Stories & Tasks)
             ▼
[ GITHUB: Feature Branch (feature/BLYNT-123-title) ]
             │ (Automated Webhook Sync)
             ▼
[ GITHUB ACTIONS: Quality Gate (Lint, Typecheck, 26 Test Suites / 127 Tests) ]
             │ (Pull Request Approved by 2 Senior Engineers)
             ▼
[ STAGING: Deployed via AWS App Runner / Amplify ]
```

```
              │ (QA Verification Matrix Signed Off)
              ▼
[ JIRA: Transition to DONE / RELEASED ]
              │ (Automated Sync)
              ▼
[ CONFLUENCE: Release Notes Published & Runbook Updated ]
```

1.2 Confluence as the Authoritative Single Source of Truth (SSOT)

- **The Golden Rule:** No feature code is written without an approved Confluence PRD (Product Requirements Document) or RFC (Request for Comments).
- **Contents of Confluence:** Architectural Decision Records (ADRs), mathematical formulas, statutory UK tax rules, API schemas, and incident post-mortems.

1.3 Jira as the Agile Execution Engine

- **Execution Scope:** Tracking day-to-day sprint velocity, assigning engineering ownership, enforcing code review gates, and monitoring release burn-down.
- **Sprint Cadence:** Fixed 2-week iterations starting Wednesday 10:00 UTC and closing Tuesday 17:00 UTC.

1.4 Bi-Directional Linking Strategy

- Every Jira Epic must contain a direct hyperlink to its parent Confluence PRD.
- Every GitHub pull request must include the Jira issue key in its title and branch name (`feature/BLYNT-104-sales-tax-calc`).
- When the pull request is merged, Jira automatically marks the story as `QA / TESTING` or `DONE`.

2. Issue Hierarchy & The 50-Phase Epic Architecture

2.1 The 4-Tier Issue Hierarchy

Hierarchy Level	Issue Type	Definition & Purpose	Example
Level 1	**Initiative**	High-level strategic milestone spanning multiple quarters.	`INIT-01`: Milestone 1 — Double-Entry Core Engine
Level 2	**Epic**	Discrete engineering phase delivering end-to-end architectural capability.	`BLYNT-EPIC-10`: Phase 10 — Sales Invoicing & Billing
Level 3	**Story / Task / Bug**	Work item deliverable	`BLYNT-142`: "Implement

		within a single 2-week sprint.	20% UK VAT calculation in MoneyService"
Level 4	**Sub-Task**	Technical task completed by a single developer in < 1 day.	`BLYNT-143`: "Write unit tests in money.service.spec.ts"

2.2 Mapping the 50 Phases into Jira Epics

Every phase in the blynt roadmap maps 1:1 to a formal Jira Epic:

Milestone 1: Double-Entry Core Engine (Completed & Verified)

- `BLYNT-EPIC-01`: Phase 1 — Project & Database Foundation
- `BLYNT-EPIC-02`: Phase 2 — Authentication & Sessions
- `BLYNT-EPIC-03`: Phase 3 — Multi-Organisation Management
- `BLYNT-EPIC-04`: Phase 4 — Roles & Permissions (RBAC)
- `BLYNT-EPIC-05`: Phase 5 — Chart of Accounts & Seed Data
- `BLYNT-EPIC-06`: Phase 6 — Financial Years & Accounting Periods
- `BLYNT-EPIC-07`: Phase 7 — Manual Journal Entry & Multi-Line Grid
- `BLYNT-EPIC-08`: Phase 8 — Central Posting & Validation Engine (15 Invariants)

Milestone 2: Commercial Workflows & Subledgers (Active & Delivered)

- `BLYNT-EPIC-09`: Phase 9 — Contacts V2 & Subledger Architecture
- `BLYNT-EPIC-10`: Phase 10 — Sales Invoicing & Billing Auto-Posting
- `BLYNT-EPIC-11`: Phase 11 — Customer Statements & AR Ageing
- `BLYNT-EPIC-12`: Phase 12 — Purchase Bills & Accounts Payable Subledger
- `BLYNT-EPIC-13`: Phase 13 — Customer Receipts & Supplier Payments
- `BLYNT-EPIC-14`: Phase 14 — Bank Accounts & Statement Reconciliation
- `BLYNT-EPIC-15`: Phase 15 — Financial Reporting Suite V1 (TB, P&L, Balance Sheet)

Milestone 3: UK Tax Compliance & HMRC MTD Integration (Planned Q1 2027)

- `BLYNT-EPIC-16`: Phase 16 — UK 9-Box VAT Return Calculation
- `BLYNT-EPIC-17`: Phase 17 — HMRC MTD Direct API Integration
- `BLYNT-EPIC-18`: Phase 18 — Year-End Close Automation & Retained Earnings
- `BLYNT-EPIC-19`: Phase 19 — Fixed Asset Register & Depreciation
- `BLYNT-EPIC-20` to `BLYNT-EPIC-25`: CIS Reverse Charge, Practice Portal, FRS 105

Milestone 4: Advanced Operations, AI & Ecosystem (Planned Q2 2027+)


- `BLYNT-EPIC-26` to `BLYNT-EPIC-30`: UK Open Banking Live Bank Feeds (TrueLayer/Plaid)
- `BLYNT-EPIC-31` to `BLYNT-EPIC-35`: AI Receipt OCR & Document Extraction
- `BLYNT-EPIC-36` to `BLYNT-EPIC-40`: Machine Learning Nominal Code Categorization

- `BLYNT-EPIC-41` to `BLYNT-EPIC-45`: Multi-Currency Accounting & FX Revaluations
- `BLYNT-EPIC-46` to `BLYNT-EPIC-50`: Intercompany Consolidation & Group Accounts

3. The Jira Issue Lifecycle & State Machine

Every Jira issue moves through a strict 6-stage lifecycle governed by automated transition validators.

3.1 State Transition Definitions & Progression Rules

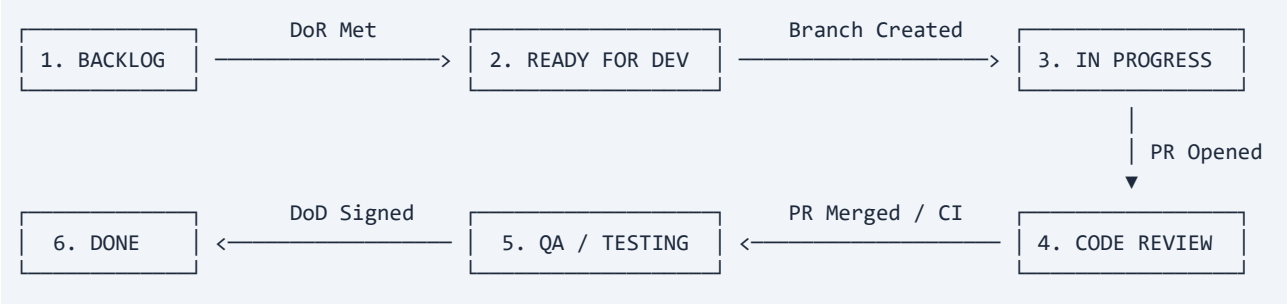

1. **`BACKLOG`:** Work item captured, preliminary scope drafted. Not estimated or committed.
2. **`READY FOR DEVELOPMENT`:**
   - **Transition Validator:** Requires linked Confluence PRD, clear Gherkin acceptance criteria, and Story Point estimation.
   - **Assignee:** Assigned to engineer during Sprint Planning.
3. **`IN PROGRESS`:**
   - **Transition Validator:** Developer creates Git branch named `feature/BLYNT-XXX-description`.
   - Only one issue in progress per developer at any given time (WIP limit = 1).
4. **`CODE REVIEW`:**
   - **Transition Validator:** Pull Request opened against `develop`.
   - Automated CI pipeline triggered in GitHub Actions.
   - Requires 2 approvals from Senior Engineers. Zero unresolved comments.
5. **`QA / TESTING`:**
   - **Transition Validator:** PR merged to staging branch. Code deployed to AWS Staging.
   - QA engineer executes manual test cases and automated regression suite.
6. **`DONE / RELEASED`:**
   - **Transition Validator:** Production deployment verified, release notes recorded in Confluence, user documentation updated.

3.2 The Hotfix & Emergency Incident Workflow (SEV-1 / SEV-2)

When an accounting drift or production outage occurs:

```
[ PagerDuty Alert / Incident Raised ]
                  │
                  ▼
[ JIRA: Bug Created with Severity = SEV-1 ]
                  │
                  ▼
[ Auto-Slack Channel Created: #incident-blynt-123 ]
                  │
                  ▼
[ Git Branch Created: hotfix/BLYNT-123-emergency-patch ]
                  │
                  ▼
[ Emergency PR Gate: Requires Lead Architect + IC Approval ]
                  │
                  ▼
[ Direct Production Deploy via AWS App Runner ]
                  │
                  ▼
[ CONFLUENCE: Post-Mortem Report Generated within 24 Hours ]
```

4. Quality Gatekeepers: Definition of Ready & Definition of Done

4.1 Definition of Ready (DoR) Gatekeeper Checklist

Before an item can transition from `BACKLOG` to `READY FOR DEV`:

- [ ] **Business Value Clear:** User story follows standard format: *"As a [Role], I want [Feature] so that [Benefit]"*.
- [ ] **Gherkin Acceptance Criteria:** At least two acceptance scenarios documented using `Given-When-Then`.
- [ ] **Confluence Link:** Direct link to approved PRD in Confluence Space `PROD`.
- [ ] **Accounting Invariant Check:** Any change to debit/credit handling verified by Lead Accountant.
- [ ] **Story Point Sized:** Estimated using Fibonacci scale by at least 3 team members.
- [ ] **No Blocking Dependencies:** All upstream APIs or database migrations are complete.

4.2 Pull Request Quality Gate & CI Automation

Before code can be merged into `develop` or `main`:

- [ ] Branch name formatted as `feature/BLYNT-XXX-slug` or `bugfix/BLYNT-XXX-slug`.

- [ ] Pull request description links to Jira issue key.
- [ ] **Automated CI Checks PASS:**
- `npm audit`: Zero high or critical vulnerabilities.
- `npx prisma validate`: Database schema compiles without error.
- `npm run lint`: Zero ESLint warnings or errors.
- `npm run typecheck`: TypeScript compilation succeeds without errors.
- **Unit & Service Tests:** All 26 test suites (127 active tests) pass.
- [ ] Code coverage does not decrease.
- [ ] Two peer code review approvals from designated Senior Engineers.

4.3 Definition of Done (DoD) Sign-Off Criteria

Before an issue is closed as `DONE`:

- [ ] Code merged to `main` branch.
- [ ] Deployed to AWS Staging and verified by QA.
- [ ] API endpoints documented in OpenAPI / Swagger (`/api/v1/docs`).
- [ ] Confluence documentation updated in Space `ENG` or `PROD`.
- [ ] Audit log events verified for any new mutating action.

5. Confluence Space Architecture & Page Templates

5.1 Confluence Space Structure

Space Key	Space Name	Purpose & Primary Contents	Space Admins
`ENG`	**Engineering & Architecture**	Architecture blueprints, ADRs, database schemas, API specs, developer onboarding.	Lead Architect
`PROD`	**Product Management**	Product Requirement Documents (PRDs), user personas, 50-phase roadmap, competitive benchmarks.	Product Owner
`QA`	**Quality Assurance**	Test strategies, regression test matrices, automated test execution reports.	QA Lead
`SEC`	**Security & Compliance**	Statutory UK HMRC MTD	Compliance Lead

		certification records, SOC 2 / ISO 27001 policies, audit trail proofs.	
`OPS`	**Site Reliability & Operations**	Disaster recovery runbooks, AWS infrastructure playbooks, incident post-mortems.	Lead SRE

5.2 Standard Product Requirement Document (PRD) Template

Used for every Phase Epic in Confluence Space `PROD`:

```
# [PRD] Phase XX: [Feature Title]

**Status:** APPROVED
**Author:** Product Owner
**Jira Epic:** BLYNT-EPIC-XX
**Target Milestone:** Milestone X (Q1 2027)

## 1. Problem Statement & Business Opportunity
* What customer problem does this phase solve?
* What statutory UK tax or accounting regulation requires it?

## 2. User Personas & Permissions
* Which roles (OWNER, ACCOUNTANT, BOOKKEEPER) have access?

## 3. Functional Requirements & Gherkin Scenarios
* Scenario 1: Successful Posting
  * Given an invoice with subtotal £100 and VAT rate 20%
  * When the accountant clicks "Approve & Post"
  * Then a journal entry with £120 debit to AR and £20 credit to VAT is posted.

## 4. Non-Functional Requirements
* Maximum API latency: < 150ms P95.
* Storage & decimal precision: NUMERIC(19,4).

## 5. Security & Audit Logging
* What AuditLog eventType is emitted?
```

5.3 Architectural Decision Record (ADR) Template

Recorded in Confluence Space `ENG` whenever an architectural standard is adopted:

```
# ADR-008: Adoption of Decimal.js for Fixed-Point Financial Math

**Date:** 2026-10-10
**Status:** ACCEPTED
**Deciders:** Lead Architect, Senior Backend Engineer

## Context
```

```
JavaScript native floating-point numbers (IEEE 754) produce rounding artifacts (e.g. 0.1 + 0.2 =
0.30000000000000004) that violate statutory accounting invariants.

## Decision
We wrap Decimal.js inside a dedicated `MoneyService` configuring 4 decimal places of fixed-point
precision matching PostgreSQL `NUMERIC(19,4)`.

## Consequences
* **Positive:** Zero financial drift; exact debit/credit equality verification.
* **Negative:** Requires converting Prisma Decimal types into MoneyService instances before
arithmetic operations.
```

6. Agile Ceremonies, Story Point Estimation & Sprint Cadence

6.1 2-Week Sprint Schedule & Cadence

```
Week 1 - Wednesday (10:00 UTC): Sprint Planning (Committing sprint backlog)
Week 1 - Daily (09:30 UTC): Standup (15 mins: Done yesterday, Doing today, Blockers)
Week 1 - Thursday (14:00 UTC): Backlog Refinement & Story Pointing (Sprint N+1)
Week 2 - Daily (09:30 UTC): Standup
Week 2 - Tuesday (15:00 UTC): Sprint Demo & Review (Showcase to stakeholders)
Week 2 - Tuesday (16:00 UTC): Sprint Retrospective (Start, Stop, Continue)
Week 2 - Tuesday (17:00 UTC): Sprint Closure & Deployment Release Cut
```

6.2 Story Pointing & Modified Fibonacci Sizing

Story Points	Complexity Level	Typical Scope & Effort
1 Point	Trivial	Text change, config flag update, simple unit test addition (< 2 hours).
2 Points	Small	Minor bug fix, small API validation tweak, UI button styling (half-day).
3 Points	Medium	Standard CRUD endpoint, new DTO with class-validator, simple UI modal (1 day).
5 Points	Large	Complex business logic, service with transaction locks, multi-line UI grid (2–3 days).
8 Points	Very Large	Major accounting engine module, new subledger pipeline, complex report generation (1 week).

13+ Points	Epics	**Too large for a single story.** Must be decomposed into smaller user stories.

7. Jira Smart Automations & Webhooks

The blynt project utilizes six production Jira automation rules:

Rule Name	Trigger Event	Condition	Action Executed
Rule 1: Auto In-Progress	GitHub: Branch created	Issue in `READY FOR DEV`	Transition issue to `IN PROGRESS`. Assign to branch creator.
Rule 2: Auto Code Review	GitHub: Pull Request opened	Issue in `IN PROGRESS`	Transition issue to `CODE REVIEW`. Add comment linking PR URL.
Rule 3: Auto QA Testing	GitHub: PR merged to `develop`	Issue in `CODE REVIEW`	Transition issue to `QA / TESTING`. Notify QA Lead.
Rule 4: Auto Done Release	AWS: Production deployment event	Issue in `QA / TESTING`	Transition issue to `DONE`. Set `fixVersion` to release tag.
Rule 5: SEV-1 Alerting	Jira: Bug created with `Priority = Highest`	Issue Type = `Bug`	Send immediate alert to Slack `#war-room-blynt` and page on-call engineer.
Rule 6: Auto-Close Sub-tasks	Jira: Parent issue transitioned to `Done`	All sub-tasks unresolved	Automatically transition all child sub-tasks to `Done`.

END OF BLYNT JIRA & CONFLUENCE AGILE WORKFLOW SPECIFICATION
